



Obsolete Pesticides Management Project (P131778)

AFRICA | Cote d'Ivoire | Environment & Natural Resources Global Practice |
Global Environment Project | Investment Project Financing | FY 2016 | Seq No: 8 | ARCHIVED on 10-Jun-2019 | ISR37207 |

Implementing Agencies: Ministry of Environment, Urban Health and Sustainable Development, Ministry of Economy and Finances

Key Dates

Key Project Dates

Bank Approval Date: 25-Aug-2015

Effectiveness Date: 19-Jan-2016

Planned Mid Term Review Date: 12-Nov-2018

Actual Mid-Term Review Date: 13-May-2019

Original Closing Date: 30-Oct-2020

Revised Closing Date: 30-Oct-2020

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The Project Development Objective (PDO) is to improve the management of obsolete pesticides and associated wastes in Côte d'Ivoire by the Government and other stakeholders.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Regulatory and institutional framework:(Cost \$1.90 M)

Management of obsolete pesticides and associated wastes:(Cost \$6.50 M)

Promotion of alternatives to chemical pesticides:(Cost \$0.70 M)

Project management:(Cost \$1.70 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Moderately Satisfactory	● Moderately Unsatisfactory
Overall Implementation Progress (IP)	● Moderately Satisfactory	● Moderately Unsatisfactory
Overall Risk Rating	● Substantial	● Substantial

Implementation Status and Key Decisions

The MTR covers the period up to May 2019. Project activities in all components of the project are ongoing.

- The Project has made some significant advancements: (i) draft regulatory texts have been prepared and will be forwarded to MINEDD and submitted to Parliament in the second semester of 2019; those texts are: a) a bill to enumerate infractions and sanctions involving usage of obsolete pesticides and associated wastes; b) a decree regulating the possession, transport, storage and disposal of pesticides; c) a decree establishing, allocating, organizing and operating a public institution called the Anti-Poison and Toxico-Vigilance



Center; and d) an inter-ministerial decree establishing a procedure for the management of seized pesticides; (ii) 108 Departmental Committees for the Control of Illegal Pesticides (CDLPI) are functional; (iii) the inventory of obsolete pesticides has been completed and a web-enabled pesticides management system--the first of its kind in West Africa--has been created.

- However, at the end of the mid-term review, the project had achieved 64% of its activities. Increased proactivity on the part of the Government is necessary to bring these activities to their fruitful conclusion. Delays in funding have had knock-on effects, pushing back the project's timetable and causing money intended for specified sub-components to be diverted to others. The Government's financial contribution will need to be provided as soon as is possible to enhance the potential of achieving project objectives by project closure.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● Moderate	● Moderate	● Moderate
Macroeconomic	● Low	● Low	● Low
Sector Strategies and Policies	● Low	● Low	● Low
Technical Design of Project or Program	● Moderate	● Moderate	● Moderate
Institutional Capacity for Implementation and Sustainability	● Substantial	● Substantial	● Substantial
Fiduciary	● Moderate	● Substantial	● Substantial
Environment and Social	● Substantial	● Substantial	● Substantial
Stakeholders	● Moderate	● Moderate	● Moderate
Other	--	--	--
Overall	● Substantial	● Substantial	● Substantial

Results

PDO Indicators by Objectives / Outcomes

Improved management of obsolete pesticides and associated wastes				
►Data on OPs and associated wastes publicly accessible (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	01-Jul-2015	30-Jun-2017	13-May-2019	30-Oct-2020
Comments:	Information on this indicator will be available in the third quarter of 2019. The validation and processing of data from the national OPAW (Obsolete Pesticides and Associated Waste) inventory is ongoing and is expected to be completed in July 2019.			
►POPs & POPs waste destroyed, disposed or contained in an environmentally sound manner (Metric ton, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	0.00	0.00	250.00
Date	01-Jul-2015	30-Jun-2017	13-May-2019	30-Oct-2020
Comments:	There are 228 tonnes of obsolete pesticides and 20 tonnes of associated waste inventoried out of 4,790 warehouses. It is now a matter of characterizing these OPAWs. Reconfirmation of OPAW quantities will be done by inventory agents.			
▲OPs and associated waste safely contained at targeted sites (Metric ton, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100.00
Date	01-Jul-2015	29-Jun-2018	13-May-2019	30-Oct-2020
▲OPs and associated waste safely disposed of (Metric ton, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	150.00
Date	01-Jul-2015	29-Jun-2018	13-May-2019	30-Oct-2020
Benefits of improved management accrue to all stakeholders				
►Direct project beneficiaries (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	7,226.00	51,348.00	100,000.00
Date	01-Jul-2015	29-Jun-2018	13-May-2019	30-Oct-2020
Comments:	The information collected on this indicator will be further developed after pesticide collection, storage, and commencement of pesticide alternative promotion activities have begun. The impact of securing Obsolete Pesticides on surrounding neighborhoods has not been accounted for in this data.			
▲Female beneficiaries (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	13.00	32.00	50.00

Intermediate Results Indicators by Components

Regulatory and institutional framework				
▶National strategy for management of OPs and associated wastes implemented (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	3.00
Date	01-Jul-2015	29-Jun-2018	13-May-2019	30-Oct-2020
Comments:	A draft of the national strategy for OPAW is being prepared. The document will be available during the second half of 2019.			



►Pesticides Committee functional (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	1.00	3.00	3.00	3.00
Date	01-Jul-2015	29-Jun-2018	13-May-2019	30-Oct-2020
Comments:	The Pesticides Committee is fully functional and fulfills its responsibilities in a suitable manner. Committee meetings are held quarterly and reports are available.			
►Effective regulatory framework for obsolete pesticides and associated wastes (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	1.00	3.00
Date	01-Jul-2015	29-Jun-2018	13-May-2019	30-Oct-2020
Comments:	The draft laws have been validated and are available. These projects will be sent to MINEDD in the first quarter of 2019.			
Management of obsolete pesticides and associated wastes				
►Inventory of obsolete pesticides and associated wastes (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2.00	3.00	3.00
Date	01-Jul-2015	29-Jun-2018	13-May-2019	30-Oct-2020
Comments:	The national pesticide inventory has been completed and all inventory data has been incorporated into the database designed for this purpose.			
►MIS on obsolete pesticides and associated wastes established and functional (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	1.00	2.00	3.00
Date	01-Jul-2015	29-Jun-2018	13-May-2019	30-Oct-2020
Comments:	A web-enabled database, in which all information relating to pesticides inventoried on the national territory has been entered, has been put in place and is functional.			
Promotion of alternatives to chemical pesticides				
►Implementation of pilots on alternatives to chemical pesticides (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	1.00	3.00
Date	01-Jul-2015	29-Jun-2018	13-May-2019	30-Oct-2020
Comments:	Agreements with the Ivorian Association of Agricultural Sciences (AISA), National Laboratory for Support to Agricultural Development (LANADA) and the Center of Excellence for the Development of Biopesticides (CEA-CCBAD) have been signed to set up the field schools during 2019. A document on the technical arrangements of demonstration fields is available.			



Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P131778	TF-A0742	Effective	USD	7.00	7.00	0.00	5.01	1.99	72%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P131778	TF-A0742	Effective	25-Aug-2015	20-Oct-2015	19-Jan-2016	30-Oct-2020	30-Oct-2020

Cumulative Disbursements

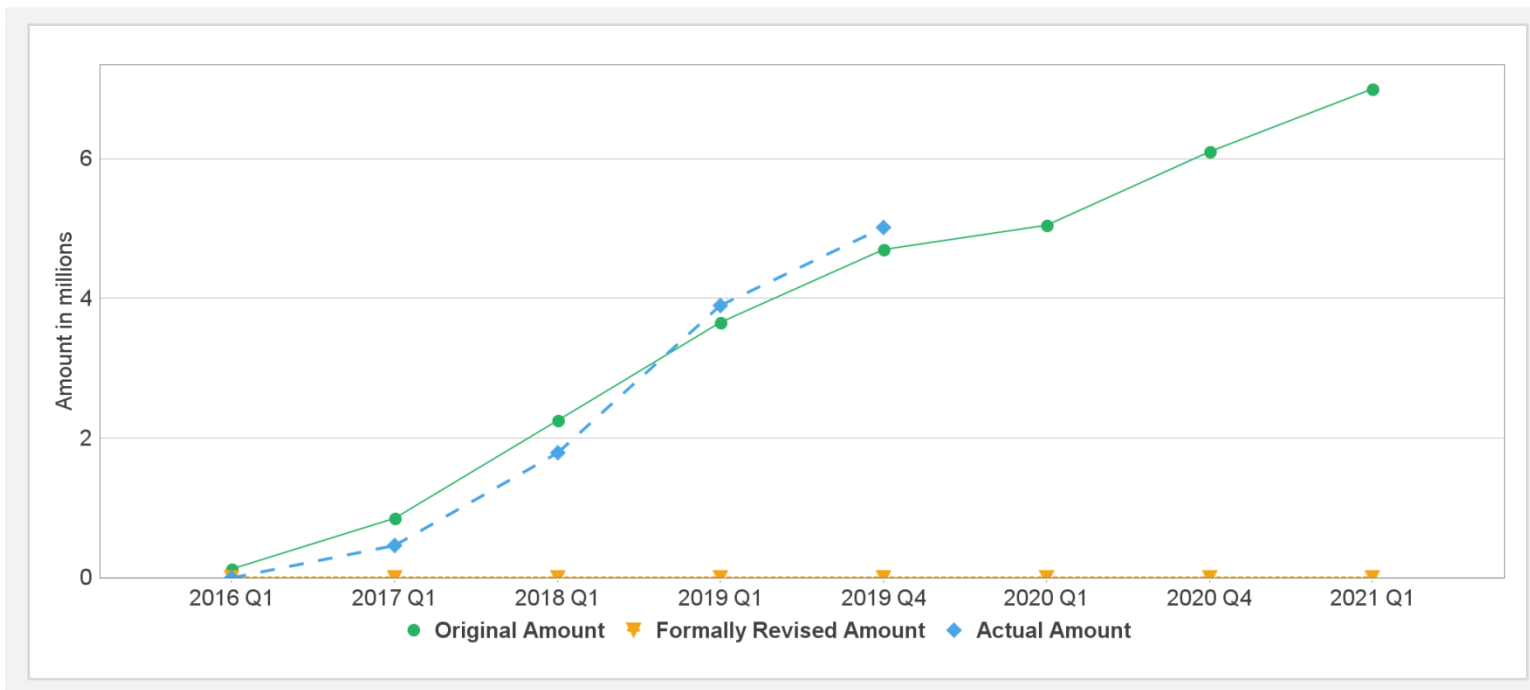

Restructuring History

There has been no restructuring to date.



Related Project(s)

There are no related projects.
