



Pacific Resilience Program (P155542)

EAST ASIA AND PACIFIC | Pacific Islands | Urban, Resilience and Land Global Practice |
IBRD/IDA | Investment Project Financing | FY 2015 | Seq No: 12 | ARCHIVED on 20-Jun-2021 | ISR47018 |

Implementing Agencies: Pacific Islands Forum Secretariat, Pacific Islands Forum Secretariat

Key Dates**Key Project Dates**

Bank Approval Date: 19-Jun-2015

Effectiveness Date: 19-Nov-2015

Planned Mid Term Review Date: 03-Dec-2018

Actual Mid-Term Review Date: 03-Dec-2018

Original Closing Date: 30-Nov-2020

Revised Closing Date: 31-Oct-2022

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To strengthen early warning, resilient investments and financial protection of the Participating Countries.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components Table

Name

Component 1: Strengthening Early Warning and Preparedness

Component 2: Mainstreaming Risk Reduction and Resilient Investments

Component 3: Disaster Risk Financing:(Cost \$0.80 M)

Component 4: Project and Program Management:(Cost \$1.42 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Risk Rating	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate

Implementation Status and Key Decisions

The project continues to provide support and coordination for both early warning and resilient investments in Pacific Island Countries (PICs) by supporting their engagement in cross-country dialogues as well as providing technical advice and support for the Framework for Resilient Development (FRDP) through many activities including the Technical Working Group and the Pacific Resilience Partnership (PRP).



Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	☐ Moderate	☐ Low	☐ Low
Macroeconomic	☐ Moderate	☐ Low	☐ Low
Sector Strategies and Policies	☐ Substantial	☐ Low	☐ Low
Technical Design of Project or Program	☐ Substantial	☐ Low	☐ Low
Institutional Capacity for Implementation and Sustainability	☐ Substantial	☐ Moderate	☐ Moderate
Fiduciary	☐ Substantial	☐ Moderate	☐ Moderate
Environment and Social	☐ Low	☐ Low	☐ Low
Stakeholders	☐ Moderate	☐ Moderate	☐ Moderate
Other	☐ Substantial	☐ Moderate	☐ Moderate
Overall	☐ Substantial	☐ Moderate	☐ Moderate

Results

PDO Indicators by Objectives / Outcomes

Strengthen early warning, resilient investments and financial protection of participating countries				
▶ Direct project beneficiaries (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	827.00	869.00	2,000.00
Date	19-Jun-2015	10-Dec-2020	17-Feb-2021	31-Oct-2022
Comments:	This indicator was revised and reflects the project's focus on knowledge-sharing rather than investments within a country as per the original target. These figures include participants that attended symposiums, workshops, meetings etc., at which the PREP RC presented and advocated for the FRDP and PRP. The end target - with the virtual meetings, continued knowledge sharing using virtual platforms - remains achievable.			
☐ Female beneficiaries (as a subset of the total number of beneficiaries) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	345.00	361.00	1,000.00
Date	19-Jun-2015	10-Dec-2020	17-Feb-2021	31-Oct-2022



Intermediate Results Indicators by Components

Component 3: Disaster Risk Financing				
► Knowledge products developed for climate and disaster risk financing (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2.00	2.00	5.00
Date	29-May-2020	10-Dec-2020	09-Jun-2021	31-Oct-2022
Comments:	This indicator was added in June 2020 as part of the restructuring. The end target - with the use virtual platforms for review and continued knowledge sharing - remains achievable with two completed, one in final stages of drafting and the last two under preparation. As of June 9, 2021, the actual reflects the completion of (i) Overview of Climate and Disaster Risk Financing Options for Pacific Island Countries and (ii) RMI Climate and Disaster Resilience Case Study. A third knowledge product is in the final stages of completion.			
► Regional Knowledge Sharing and Advisory Committee meetings held (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	4.00	6.00	6.00	12.00
Date	29-May-2020	10-Dec-2020	17-Feb-2021	31-Oct-2022
Comments:	This indicator was revised in June 2020 as part of the restructuring and reflects the project's focus on knowledge-sharing rather than investments within a country as per the original target. These figures include participants that attended symposiums, workshops, meetings etc., at which the PREP RC presented and advocated for the FRDP and PRP. The end target - with the virtual meetings, continued knowledge sharing using virtual platforms - remains achievable with two meetings (PCM and RAC) confirmed in August and September 2021 and others before project closes in Oct 2022.			

Performance-Based Conditions

Data on Financial Performance

Disbursements (by loan)


Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P155542	IDA-D0750	Effective	USD	1.32	1.32	0.00	0.95	0.47	67%
P155542	TF-A0887	Effective	USD	0.90	0.90	0.00	0.57	0.33	63%

Key Dates (by loan)



Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P155542	IDA-D0750	Effective	19-Jun-2015	21-Oct-2015	19-Nov-2015	30-Nov-2020	31-Oct-2022
P155542	TF-A0887	Effective	19-Jun-2015	21-Oct-2015	19-Nov-2015	30-Nov-2020	31-Oct-2022

Cumulative Disbursements

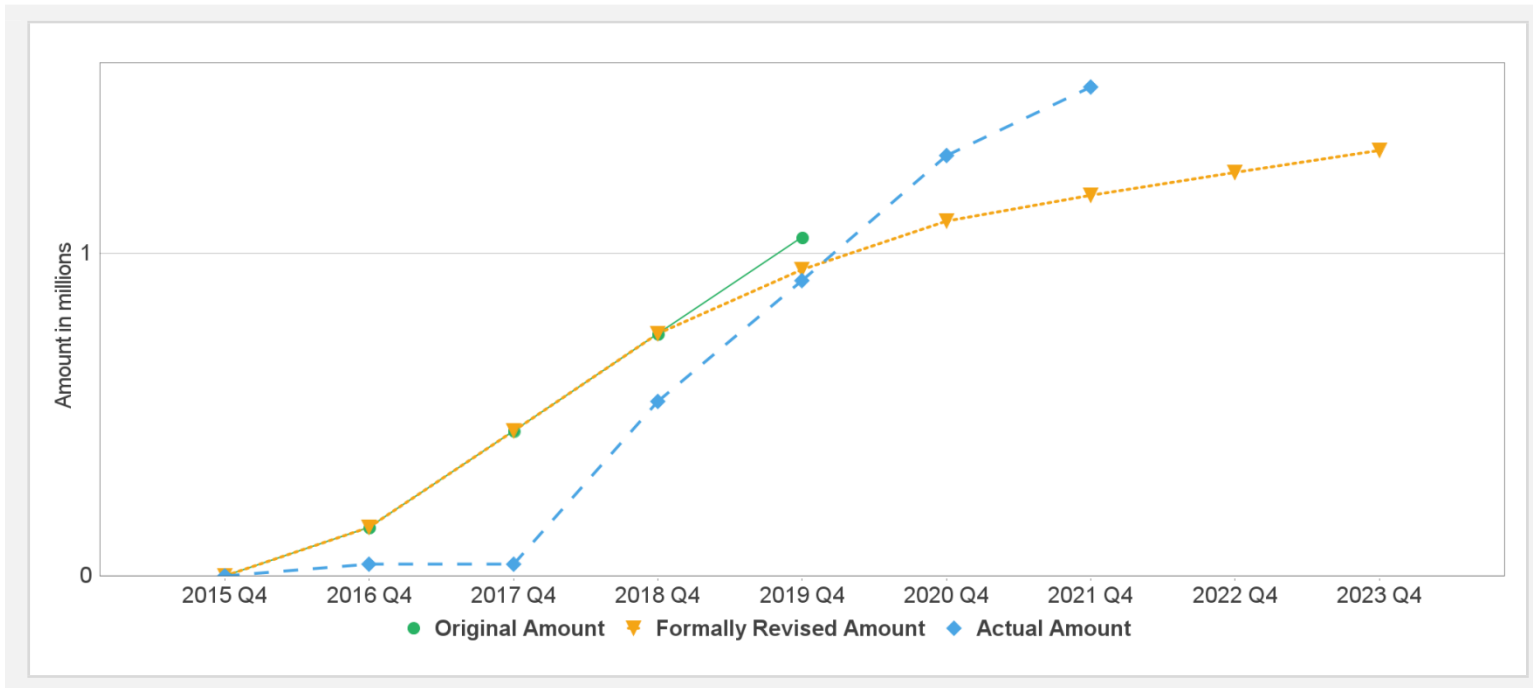

PBC Disbursement

PBC ID	PBC Type	Description	Coc	PBC Amount	Achievement Status	Disbursed amount in Coc	Disbursement % for PBC
--------	----------	-------------	-----	------------	--------------------	-------------------------	------------------------

Restructuring History

Level 2 Approved on 30-Jun-2020 ,Level Approved on 20-Jul-2020

Related Project(s)

P156335-PACIFIC RESILIENCE PROGRAM
