



## West Africa Region Fisheries Program AF Guinea, Sierra Leone &amp; Liberia (P126773)

AFRICA WEST | Western Africa | Environment, Natural Resources & the Blue Economy Global Practice | IBRD/IDA | Investment Project Financing | FY 2015 | Seq No: 13 | ARCHIVED on 25-Feb-2021 | ISR45310 |

Implementing Agencies: Ministry of Fisheries and Maritime Economy, Ministry of Fisheries and Aquaculture, Ministry of Finance, Ministry of Economic Affairs and Development

**Key Dates****Key Project Dates**

Bank Approval Date: 16-Mar-2015

Effectiveness Date: 24-Jun-2015

Planned Mid Term Review Date: 20-Mar-2018

Actual Mid-Term Review Date: 20-Mar-2018

Original Closing Date: 15-Dec-2020

Revised Closing Date: 31-Dec-2021

**Project Development Objectives**

Project Development Objective (from Project Appraisal Document)

The development objective of this first phase of the West Africa Regional Fisheries Program SOP-C (formerly APL-C) is to strengthen governance and management of targeted fisheries and improve handling of landed catch at selected sites.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

**Components Table**

Name

Strengthening Good Governance and Sustainable Management of the Fisheries:(Cost \$10.40 M)

Reducing Illegal, Unreported and Unregulated Fishing:(Cost \$3.02 M)

Increasing Contribution of the Fish Resources to the Local Economy:(Cost \$9.48 M)

Project Management, Monitoring and Evaluation, and Regional Coordination:(Cost \$7.15 M)

**Overall Ratings**

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Risk Rating	<input type="checkbox"/> Substantial	<input type="checkbox"/> Moderate

**Implementation Status and Key Decisions**

Overall there is good progress and tangible results. Disbursement grew +20% through CY2020 but COVID is impacting this momentum. To address the impact of the sanitary crisis, the Project was granted a one-year extension until Dec. 31, 2021.

For **Mauritania**, Implementation of Component 3 (Rehabilitation of Fish Market in Nouakchott) has picked up, notably with Lot 1 being completed and accepted and construction under Lot 2 having started. However work is slowed due to the COVID pandemics. Under component 1 (Strengthening good governance and sustainable management of fisheries), many activities are coming to an end with their expected results, demonstrating that the PRAO-MR has effectively contributed to the advancement of scientific knowledge (e.g., monthly campaigns targeted at



octopus, the results of which allow the adjustment of technical measures in near-real time, such as time-area closures for the protection of juveniles); strengthening regulatory and institutional framework (e.g., support to the new strategy of the sector or the adoption of management plans for two priority fisheries); or better monitoring of the fisheries (electronic logbook of the fisheries in force). Registration of canoes has also finally resumed.

For **Guinea**, the pace of project implementation allowed the achievement of most of the Project's intermediate result indicators during 2020 and only few activities need to be completed in order to achieve development objectives of the project including finalization of the access road to the Koukoude's artisanal landing site and repair of the main patrol vessel to increase high-sea industrial fisheries surveillance. Beyond the implementation of these activities, the last year of the project is dedicated to (i) the implementation of a technical capacity building program to finalize MPAEM reform and (ii) the development of a strategy and investment plan for the sector capitalizing on the achievements of the project. For **Sierra Leone**, 60% of PDO-level indicators are achieved, and remaining 40% are on track to being achieved with some expedited implementation. Industrial fishing effort reduction to help recover the fish stock is showing signs of improvement with foreign industrial trawler numbers in January 2021 reduced to 43 from 68 in May 2020. The slowdown in implementation of activities, some of which are attributed to COVID-19 reported in June 2020 continues to impact project implementation. Despite delays in planning and decisions pertaining to new activities post restructuring by MFMR, all project funds are now committed.

## Risks

### Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial	<input type="checkbox"/> Moderate
Macroeconomic	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Sector Strategies and Policies	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Technical Design of Project or Program	<input type="checkbox"/> Moderate	<input type="checkbox"/> Low	<input type="checkbox"/> Low
Institutional Capacity for Implementation and Sustainability	<input type="checkbox"/> High	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Fiduciary	<input type="checkbox"/> High	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Environment and Social	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Stakeholders	<input type="checkbox"/> Substantial	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Other	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial	<input type="checkbox"/> Moderate
Overall	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial	<input type="checkbox"/> Moderate

## Results

### PDO Indicators by Objectives / Outcomes

Strengthen governance & mgmt of targeted fisheries and improve handling of landed catch at sltd site				
► Share of fisheries management data published regularly and made publicly accessible - GN (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	83.00	83.00	83.00
Date	01-Jul-2014	01-Sep-2019	15-Dec-2020	15-Dec-2020



► Share of fisheries management data published regularly and made publicly accessible--SL (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	25.00	50.00	100.00
Date	08-Feb-2017	15-Nov-2019	31-Dec-2020	31-Dec-2021
► Share of fisheries management data published regularly and made publicly accessible - MR (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	42.00	66.00	83.00
Date	01-Jul-2014	01-Sep-2019	12-Oct-2020	15-Dec-2020
Comments:	Electronic logbook system (JEP, journal électronique de pêche) have been installed on most of the national vessels, and the training to the captains and the operators was conducted in May 2019. The rest of national vessels will have JEP in coming months, to have full coverage on national vessels. Having JEP system in all vessels is expected to contribute in having on-time data.			
► Number of fishing vessels operating in the exclusive economic zones should not exceed the ceiling established for each segment (disaggregated by country and by segment) - GN (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Yes	Yes	Yes	Yes
Date	01-Jul-2014	01-Sep-2019	15-Dec-2020	15-Dec-2020
Comments:	GN: The number of registered industrial vessels is 61, the number of registered Advanced artisanal canoes (PAA, pêche artisanal avancé) is 59 and the number of registered artisanal canoes is 8862, which is lower than the ceiling of 10,000.			
► Number of fishing vessels operating in the exclusive economic zones should not exceed the ceiling established for each segment - MR (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Yes	Yes	Yes	Yes
Date	01-Jul-2014	01-Sep-2019	12-Oct-2020	15-Dec-2020
► Individual quotas in octopus are distributed to all the segment in a participatory, transparent and scientific manner - MR (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2.00	2.00	3.00
Date	01-Jul-2014	01-Sep-2019	12-Oct-2020	15-Dec-2020
Comments:	It was developed in transparent and scientific manner. Participation by artisanal segment could be strengthened in the future, so that the score can be full with 3 in the future.			
► Share of fishing vessels inspected by the national fisheries surveillance agency for compliance with national regulations - GN (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	25.00	83.00	85.00	80.00
Date	01-Jul-2014	01-Sep-2019	15-Dec-2020	15-Dec-2020
Comments:	The number of inspected vessels is expected to increase towards the end of the year. From January to March 2019. 52 vessels among 61 licensed vessels were inspected.			
<b>► Volume processing capacity according to improved hygiene condition - GN (Metric ton, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00
Date	01-Jul-2014	01-Sep-2019	15-Dec-2020	15-Dec-2020
Comments:	Koukoude landing site and smoking facility are operational but the access road is not yet finalized			
<b>► Volume processing capacity according to improved hygiene condition - MR (Metric ton, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	99.00	70.00	30.00
Date	01-Jul-2014	01-Sep-2019	12-Oct-2020	15-Dec-2020
<b>► Direct project beneficiaries (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	62,000.00	4,804,000.00	82,000.00
Date	01-Jul-2014	10-Jun-2019	15-Dec-2020	15-Dec-2020
Comments:	Guinea: 48,804 beneficiaries (artisanal fishermen 2135, smoking facility workers 984, dry fish worker 640, artisanal retailers 456, local authorities 63, artisanal pirogues registration beneficiaries 32,000, income generating activities beneficiaries 12,526)			
<input type="checkbox"/> Female beneficiaries - MR (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	23.00	9.00	30.00
Date	01-Jul-2014	01-Sep-2019	12-Oct-2020	15-Dec-2020
<input type="checkbox"/> Female Beneficiaries - GN (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	9.00	23.00	9.00
Date	01-Jul-2014	01-Sep-2019	15-Dec-2020	15-Dec-2020
<input type="checkbox"/> Direct project beneficiaries - MR (Number, Custom Breakdown)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	14,000.00	32,968.00	50,000.00
Date	01-Jul-2014	01-Sep-2019	12-Oct-2020	15-Dec-2020
<input type="checkbox"/> Direct project beneficiaries - GN (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	36,278.00	36,278.00	32,000.00
Date	01-Jul-2014	01-Sep-2019	01-Sep-2019	15-Dec-2020
<input type="checkbox"/> Number of licensed fishing vessels operating in the exclusive economic zones should not exceed the ceiling established--SL (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	114.00	127.00	43.00	97.00
Date	08-Feb-2017	15-Nov-2019	31-Dec-2020	31-Dec-2021
Comments:	The achievement in the year 2020 (47) is for the industrial trawling fleet only (does not include the tuna fleet)			
<input type="checkbox"/> Share of fishing vessels inspected by the national fisheries surveillance authority for compliance with national regulations--SL (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	35.00	45.00	50.00	70.00
Date	08-Feb-2017	15-Nov-2019	31-Dec-2020	31-Dec-2021

### Intermediate Results Indicators by Components

Strengthening Good Governance and Sustainable Management of the Fisheries				
<input type="checkbox"/> Reliable fisheries management data regularly available - GN (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	5.00	5.00	5.00
Date	01-Jul-2014	01-Sep-2019	15-Dec-2020	15-Dec-2020
Comments:	GN: 5 variables of 6 are published (available at the website of Ministry of Fisheries Aquaculture and Maritime Economy in Guinea) because no fisheries agreement are signed yet. Variables published : 1) list of valid vessel licenses in industrial segment, 2) list of artisanal fisheries vessels / canoe, 3) fees from licenses, 4) list of infractions in industrial segment, 5) fees from infractions Variables not yet published : 6) fees from fisheries agreements			
<input type="checkbox"/> Reliable fisheries management data regularly available - MR (Number, Custom)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	12.00	12.00	13.00
Date	01-Jul-2014	01-Sep-2019	12-Oct-2020	15-Dec-2020
<b>► Share of fishing vessels registered (disaggregated by country and by segment) - GN (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	95.00	83.26	75.00
Date	01-Jul-2014	01-Sep-2019	15-Dec-2020	15-Dec-2020
Comments:	APEPA NGO has calculated the share of artisanal fishing vessel registered through field Census held in oct 2020			
<b>► Share of fishing vessels registered (disaggregated by country and by segment) - MR (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	100.00	66.00	90.00
Date	01-Jul-2014	01-Sep-2019	12-Oct-2020	15-Dec-2020
<b>► Proposal for institutional and functional reform submitted to Cabinet by Ministry of Fisheries - MR (Yes/No, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	Yes	Yes	Yes
Date	01-Jul-2014	01-Sep-2019	12-Oct-2020	15-Dec-2020
<b>► Revised appropriate regulations integrating (i) access management and (ii) secure fishing rights submitted to Cabinet by Ministry of Fisheries - MR (Yes/No, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	Yes	Yes	Yes
Date	01-Jul-2014	01-Sep-2019	01-Sep-2019	15-Dec-2020
<b>► Fisheries management plans developed - GN (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	1.00	1.00	1.00
Date	01-Jul-2014	01-Sep-2019	15-Dec-2020	15-Dec-2020
<b>► Fisheries management plans developed - MR (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	1.00	2.00	2.00



Date	01-Jul-2014	01-Sep-2019	12-Oct-2020	15-Dec-2020
<b>► Fisheries management data incorporated in the regional dashboard - GN (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	5.00	5.00	5.00
Date	01-Jul-2014	01-Sep-2019	15-Dec-2020	15-Dec-2020
Comments:	five variables are incorporated in the regional dashboard at Sub-Regional Fisheries Commission (SRFC or CSRP in French, Commission Sous-Regionale des Peches). 1) list of valid vessel licenses in industrial segment, 2) list /number of artisanal boats, 3) list of infractions in industrial segment, 4) fees from licences, 5) fees from infractions			
<b>□ Fisheries management data incorporated in the regional dashboard - MR (Number, Custom Breakdown)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	6.00	7.00	9.00
Date	01-Jul-2014	01-Sep-2019	12-Oct-2020	15-Dec-2020
<b>► Individual quotas in the octopus fishery are allocated in the industrial segments in a participatory, transparent, and scientific manner - MR (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2.00	2.00	3.00
Date	01-Jul-2014	01-Sep-2019	12-Oct-2020	15-Dec-2020
Comments:	The allocation of individual quotas in the octopus fishery is considered to be based on scientific recommendation and it was a participatory process which provide a score of 2. To reach score 3, the allocation needs to be made more transparent.			
<b>► Monitoring, evaluation and surveillance reports of project activity implementation by an organization are regularly published - MR (Yes/No, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Jul-2014	01-Sep-2019	12-Oct-2020	15-Dec-2020
Comments:	This is not yet due. TOR for a consultant to develop this report is cleared, thus a consultant is expected to be hired in coming months.			
<b>► Reliable fisheries management data regularly available--SL (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2.00	5.00	4.00
Date	08-Feb-2017	15-Nov-2019	31-Dec-2020	31-Dec-2021
Comments:	<ol style="list-style-type: none"> <li>1. <u>list of valid licensed fishing vessels (industrial and decked semi-industrial (monthly));</u></li> <li>2. <u>list of infractions in artisanal sector (annually);</u></li> <li>3. <u>fees from licenses (quarterly</u></li> <li>4. <u>list of licensed industrial fishing vessels with VMS and or AIS (Monthly);</u></li> </ol>			



5.list of licensed industrial fishing vessels with observers, publicly accessible in Ministry of Fisheries website (www.mfmr.gov.sl) and/or daily newspaper.

► Fisheries management plans developed --SL (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	1.00	2.00
Date	08-Feb-2017	15-Nov-2019	31-Dec-2020	31-Dec-2021

► Submission of Revised Fisheries Act and fisheries regulations to cabinet by MFMR --SL (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	Yes	Yes
Date	08-Feb-2017	15-Nov-2019	31-Dec-2020	31-Dec-2021

Comments: YES (Yes (Fisheries and Aquaculture Act 2018 and Fisheries and Aquaculture Regulations, FAO Ports States measures, NPOA for IUU fishing) Also new fisheries regulations 2019.

► Monitoring, evaluation and surveillance reports of project activity implementation by an organization are regularly published--SL (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	Yes	Yes
Date	08-Feb-2017	15-Nov-2019	31-Dec-2020	31-Dec-2021

Comments: Yes (Community surveillance Report and SIK patrols reported, and ScOP Report uploaded into IMBO website.

### Reducing Illegal, Unreported and Unregulated Fishing

► Satellite-based surveillance system for industrial fishing vessels by the national fisheries surveillance agency is functional - GN (Hours, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	8.00	24.00	24.00	24.00
Date	01-Jul-2014	01-Sep-2019	15-Dec-2020	15-Dec-2020

Comments: The new satellite-based surveillance system initiated in May 2019 is fully functional.

► Surveillance patrol of industrial fishing vessels (number of days per year) - GN (Days, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	80.00	123.00	64.00	200.00
Date	01-Jul-2014	01-Sep-2019	15-Dec-2020	15-Dec-2020

Comments: 2018: 123 days of patrols ;  
2019: 180 days of patrols;



2020: 64 days of patrols (intermediary result from January to May), the number of patrols has been reduced due to technical issues and current repair of the patrol vessel				
<b>► Surveillance patrol of artisanal fishing boats - GN (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	276.00	570.00	96.00
Date	01-Jul-2014	01-Sep-2019	15-Dec-2020	15-Dec-2020
Comments:	2018 : 276 days of patrols 2019 : 516 days of patrols 2020 : 570 days of patrols			
<b>► Licensed industrial fishing vessels installed with functional VMS and observers on board -SL (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	100.00	100.00	100.00
Date	08-Feb-2017	15-Nov-2019	31-Dec-2020	01-Mar-2021
Comments:	100 Obcom system and 100% observer except for Tuna vessels.			
<b>► Sustainable joint maritime committee operation plan is developed --SL (Yes/No, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	08-Feb-2017	15-Nov-2019	31-Dec-2020	31-Dec-2021
<b>► Surveillance patrol of industrial fishing boats (number of days per year)--SL (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	80.00	25.00	136.00	180.00
Date	08-Feb-2017	15-Nov-2019	31-Dec-2020	31-Dec-2021

#### Increasing Contribution of the Fish Resources to the Local Economy

##### ► Integrated fish handling sites built - GN (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	1.00	1.00
Date	01-Jul-2014	01-Sep-2019	15-Dec-2020	15-Dec-2020
Comments:	The Koukoude artisanal landing site and smoking facility have been built and are ready to be inaugurated.			

##### ► Integrated fish handling sites built - MR (Number, Custom)



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	01-Jul-2014	01-Sep-2019	01-Sep-2019	15-Dec-2020
<b>► Improved smoke ovens - SL (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5.00
Date	15-Nov-2019	15-Nov-2019	31-Dec-2020	31-Dec-2021

#### Component 4: Project Management, Monitoring and Evaluation, and Regional Coordination

##### ► Participating in IW meetings--SL (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	1.00	2.00	1.00
Date	08-Feb-2017	15-Nov-2019	31-Dec-2020	31-Dec-2021

##### ► Fisheries Performance Indicators annual collected - SL (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	Yes	Yes
Date	08-Feb-2017	15-Nov-2019	31-Dec-2020	31-Dec-2021

##### ► Participating in IW meetings--GN (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	1.00	2.00	1.00
Date	08-Feb-2017	01-Sep-2019	31-Dec-2020	01-Mar-2021

##### ► Fisheries Performance Indicators applied to GN (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	Yes	Yes	Yes
Date	08-Feb-2017	01-Sep-2019	15-Dec-2020	01-Mar-2021

#### Performance-Based Conditions

► PBC 1 Number of reliable fisheries management data regularly available - MR (Percentage, Intermediate Outcome, 37,500.00, 0.00%)



	Baseline	Actual (Previous)	Actual (Current)	December 2018
Value	0.00	76.90	76.90	--
Date	01-Jul-2014	12-Dec-2018	12-Dec-2018	--
Comments:	10 out of 13 indicators.			
<b>► PBC 2 Share of fisheries management data published regularly and made publicly accessible- MR (Percentage, Outcome, 40,000.00, 0.00%)</b>				
	Baseline	Actual (Previous)	Actual (Current)	December 2018
Value	0.00	33.00	33.00	--
Date	01-Jul-2014	12-Dec-2018	12-Dec-2018	--
<b>► PBC 3 Number of fishing vessels operating in the exclusive economic zones should not exceed the ceiling established for each segment - MR (Yes/No, Outcome, 100,000.00, 0%)</b>				
	Baseline	Actual (Previous)	Actual (Current)	December 2018
Value	Yes	Yes	Yes	--
Date	01-Jul-2014	12-Dec-2018	12-Dec-2018	--

## Data on Financial Performance

### Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P126773	IDA-D0390	Effective	USD	12.00	12.00	0.00	8.64	3.34	72%
P126773	IDA-D0400	Effective	USD	10.00	10.00	0.00	9.38	0.48	95%
P131327	TF-19089	Effective	USD	7.00	7.00	0.00	5.72	1.28	82%
P156759	TF-A3530	Effective	USD	5.00	5.00	0.00	4.38	0.62	88%
P156759	TF-A3532	Closed	USD	1.00	1.00	0.00	1.00	0.00	100%
P156759	TF-A3533	Effective	USD	4.00	4.00	0.00	3.20	0.80	80%


### Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P126773	IDA-D0390	Effective	16-Mar-2015	17-Apr-2015	24-Jun-2015	15-Dec-2020	31-Dec-2021
P126773	IDA-D0400	Effective	16-Mar-2015	14-Apr-2015	30-Nov-2015	15-Dec-2020	31-Dec-2021



P131327	TF-19089	Effective	16-Mar-2015	17-Apr-2015	17-Apr-2015	15-Dec-2020	31-Dec-2021
P156759	TF-A3530	Effective	24-Feb-2017	24-Feb-2017	17-Oct-2017	01-Mar-2021	31-Dec-2021
P156759	TF-A3532	Closed	08-Feb-2017	08-Feb-2017	12-Jul-2017	01-Mar-2018	01-Mar-2019
P156759	TF-A3533	Effective	08-Feb-2017	08-Feb-2017	08-Jun-2017	01-Mar-2021	31-Dec-2021

### Cumulative Disbursements

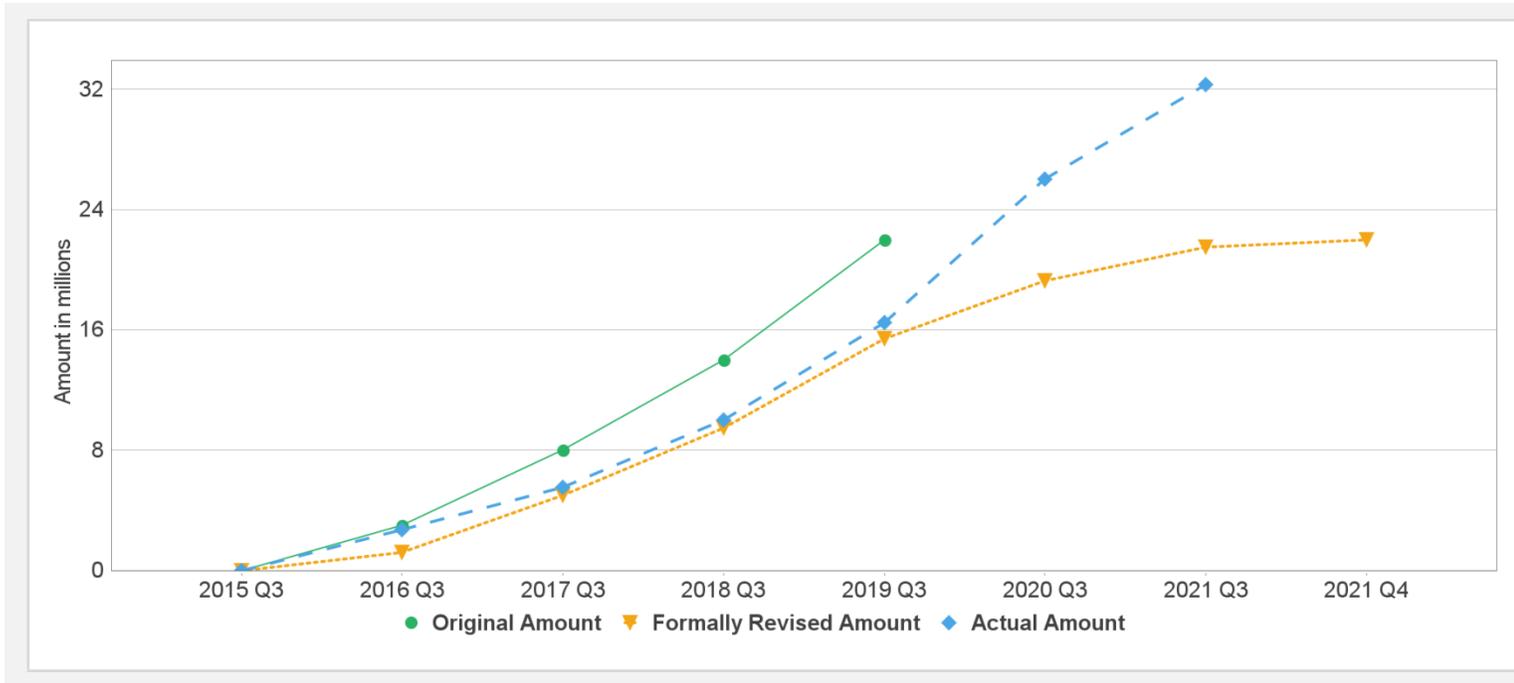

### Restructuring History

Level 2 Approved on 28-Feb-2018 ,Level 2 Approved on 30-Apr-2019 ,Level 2 Approved on 11-Jul-2020 ,Level Approved on 19-Aug-2020 ,Level 2 Approved on 28-Aug-2020 ,Level Approved on 31-Aug-2020

### Related Project(s)

P131327-West Africa - Mauritania Fish. APL
